



Big Cypress Basin Board Meeting Capital Projects Update

10/24/2013

Jeffrey Kivett, P.E., Director
Operations, Engineering and Construction Division


Miller Weir #3



Status/Schedule:

- Preliminary Design was completed on 4-30-13.
- Final Design Submittal is due in November.
- Governing Board Award of the Construction Contract is tentatively scheduled for early 2014.
- Approximate Construction Contract Duration is 365 days.

Big Cypress Basin Field Station

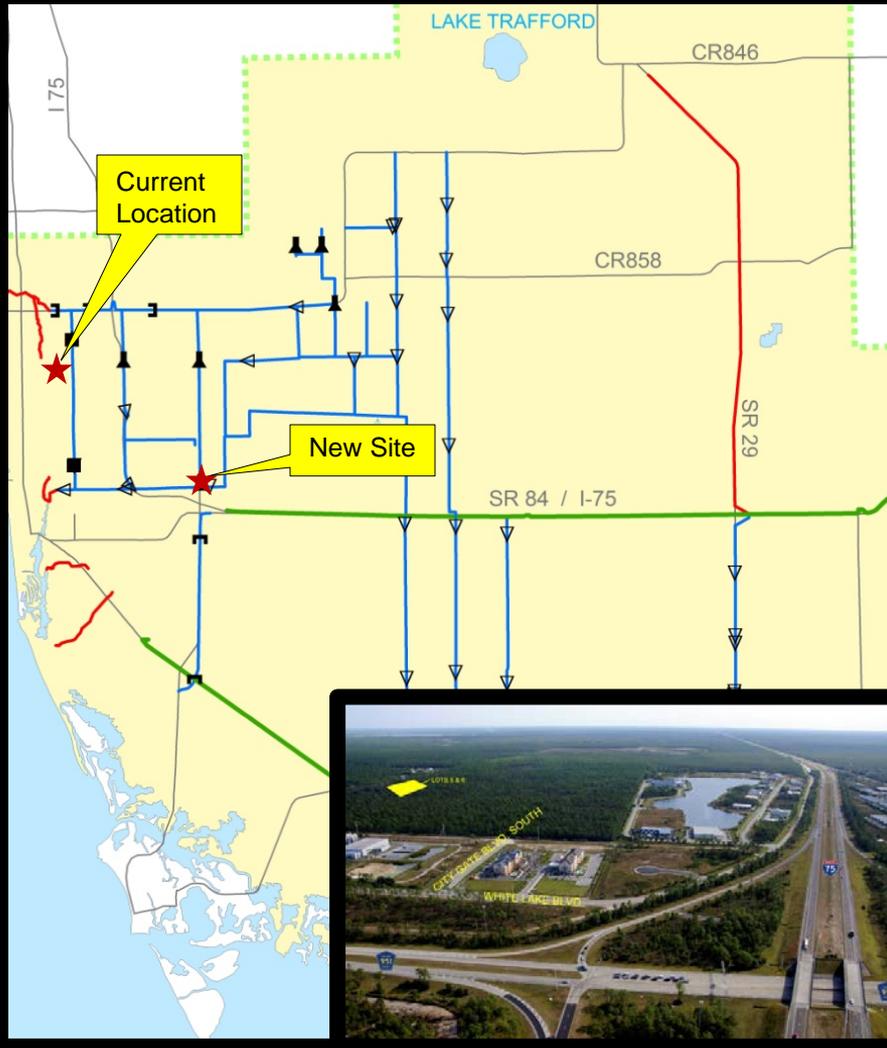

■ Progressive Design Build Contract –

- Completed Solicitation
 - DeAngelis Diamond Construction
- Starting Negotiations for Phase 1 (through 70% design)
- Phase 1 Services: October 2013 – November 2014
- Phase 2 Services (Construction Phase): November 2014 – November 2016

Big Cypress Basin Field Station

- Phase 1 Services: October 2013 – November 2014
 - Decision Point 1
 - Draft Site Analysis Technical Memo – December 2013
 - Co-Location of Service Center and Field Station
 - Decision Point 2
 - Submit 70% Design – September 2014
 - Enter into further negotiations with design / builder or execute through separate bid
- Phase 2 Services (Construction Phase): November 2014 – November 2016

Inspection Program

- Structure Inspection Program (SIP)
 - Civil, Structural, Mechanical, Electrical & Underwater Inspections
 - 5 Year Inspection Cycle
 - Structure & Inspection Data loaded to SIP Archival Tool (*online repository*)
- FY14 BCB Inspection Roster (16 Structures)
 - SR29-1, SR29-2, SR29-3, SR29-4, SR29-5, SR29-6A&B, SR29-7, SR29-8
 - GG-6&7, HC-2, I75-2&3, TwinEagle, FU1



Big Cypress Capital Projects Update

QUESTIONS?
